

N435DK "G-AMPY"

Avionics Upgrade &
Flight Deck Restoration

Weekly Progress
Update

Week of October 6, 2025





Final Panel Wiring

- Panels are undergoing final wiring.
- Brow panels are wired, to be fully installed.
- The circuit breaker panel has been installed.
- Main panels are receiving all gauges and avionics.
- The flight deck is being re-assembled.


Image: N435DK flight deck currently in-work





Weekly Highlights: Circuit Breaker Panel and Relay Panel

- The circuit breaker panel is installed.
- The relay panel has been installed and wired.
- All harnesses and bundles are all in the aircraft.
- The harnesses are receiving final extensions.

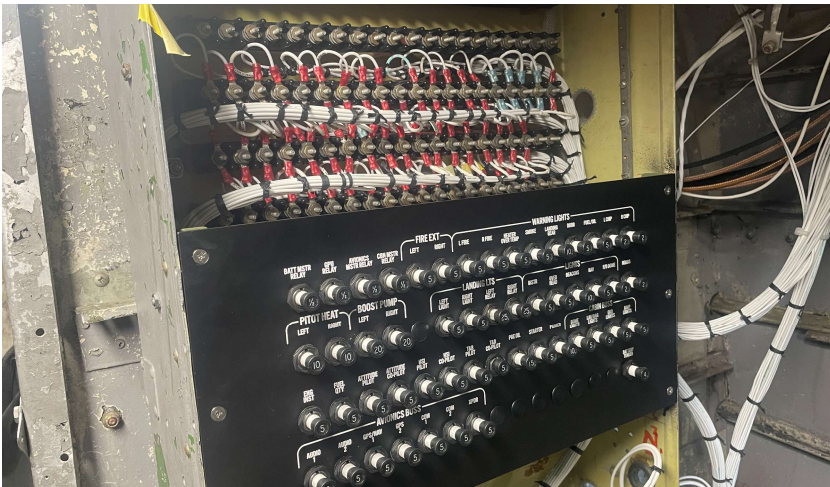

Images: N435DK circuit breakers and relays installed.





Structural Repairs

The repairs identified to make G-AMPY airworthy for flights after the avionics upgrade are complete. Several corroded stringers in the aft belly were removed, and new stringers spliced in. The team went the extra mile to consider the repairs that would ensure the most structural safety in flight.

